


CITY OF MARYSVILLE AGENDA BILL

EXECUTIVE SUMMARY FOR ACTION

CITY COUNCIL MEETING DATE: June 23, 2014

AGENDA ITEM: Project Acceptance – PUD Acquisition - 99th Ave/42nd St Water Main	
PREPARED BY: Jeff Laycock, Project Manager	DIRECTOR APPROVAL: 
DEPARTMENT: Public Works, Engineering	
ATTACHMENTS: Notice of Physical Completion Letter, Vicinity Map	
BUDGET CODE: 40220594.563000, W1102	AMOUNT: N/A

SUMMARY:

The 99th Avenue/42nd Street Water Main project was constructed as required for the City's acquisition of the PUD water system. This project included the construction of 4,850-feet of 12-inch water main from 91st Ave on 42nd Street to 99th Avenue then south on 99th Avenue connecting to the existing PUD system just south of State Route 92. Included in the project was a horizontal directional drill of a 24-inch HDPE casing and the installation of a 16-inch HDPE carrier in the portion under the new WSDOT roundabout at the intersection of SR92 and 99th Avenue.

City Council awarded the project to SRV Construction, Inc. on July 22, 2013 in the amount of \$676,425.42 including a management reserve of \$70,000.00. The management reserve was increased by an additional \$110,000 on November 25, 2013 as necessary to account for additional work associated with boring under SR 92. The total funds authorized for the project was therefore \$856,425.42. The project was completed at a cost of \$856,386.03, which was \$179,960.61 or 26.6% above the original bid amount but within the management reserve.

Work performed under this contract was inspected by City staff, the Snohomish County PUD, Snohomish County and the City of Lake Stevens under their associated right-of-way permits. The work was found to be physically complete in accordance with the approved plans and specifications. Staff recommends Council's acceptance of the project for closeout.

RECOMMENDED ACTION:
Staff recommends that Council authorize the Mayor to accept the 99th Ave/42nd St Water Main project, starting the 45-day lien filing period for project closeout.



PUBLIC WORKS
Kevin Nielsen, *Director*

80 Columbia Avenue
Marysville, Washington 98270
Phone (360) 363-8100
Fax (360) 363-8284

May 8, 2014

SRV Construction, Inc.
PO Box 481
Oak Harbor, WA 98277

Subject: 99th Avenue and 44th Street Water Main Extension Project – Notice of Physical Completion

Dear Mr. Snyder:

In accordance with the contract, the 99th Avenue and 44th Street Water Main Extension project was considered physically complete as of Friday, May 2, 2014.

Please submit your final pay request to me as soon as possible, including any tonnage tickets for HMA and the force account sheets for the crack sealing. I will also require intents for your striping and crack sealing subcontractor prior to payment.

This notification does not constitute final acceptance. Recommendation for final acceptance will be sent to the City Council for approval at the first available council meeting. This date of final acceptance shall start the forty-five (45) day lien period for the release of your retainage upon receipt of the following.

1. Certificate of Release from the Department of Revenue
2. Certificate of Release from the Employment Security Department
3. Certificate of Release from the Department of L&I
4. Affidavit of Wages Paid (to be submitted by SRV to the City)


Thank you for working with the City in the successful completion of this project.

Sincerely,

A handwritten signature in blue ink, appearing to read "Jeff Laycock".

Jeff Laycock, PE
Project Manager

99th Ave/42nd St Water Main Vicinity Map

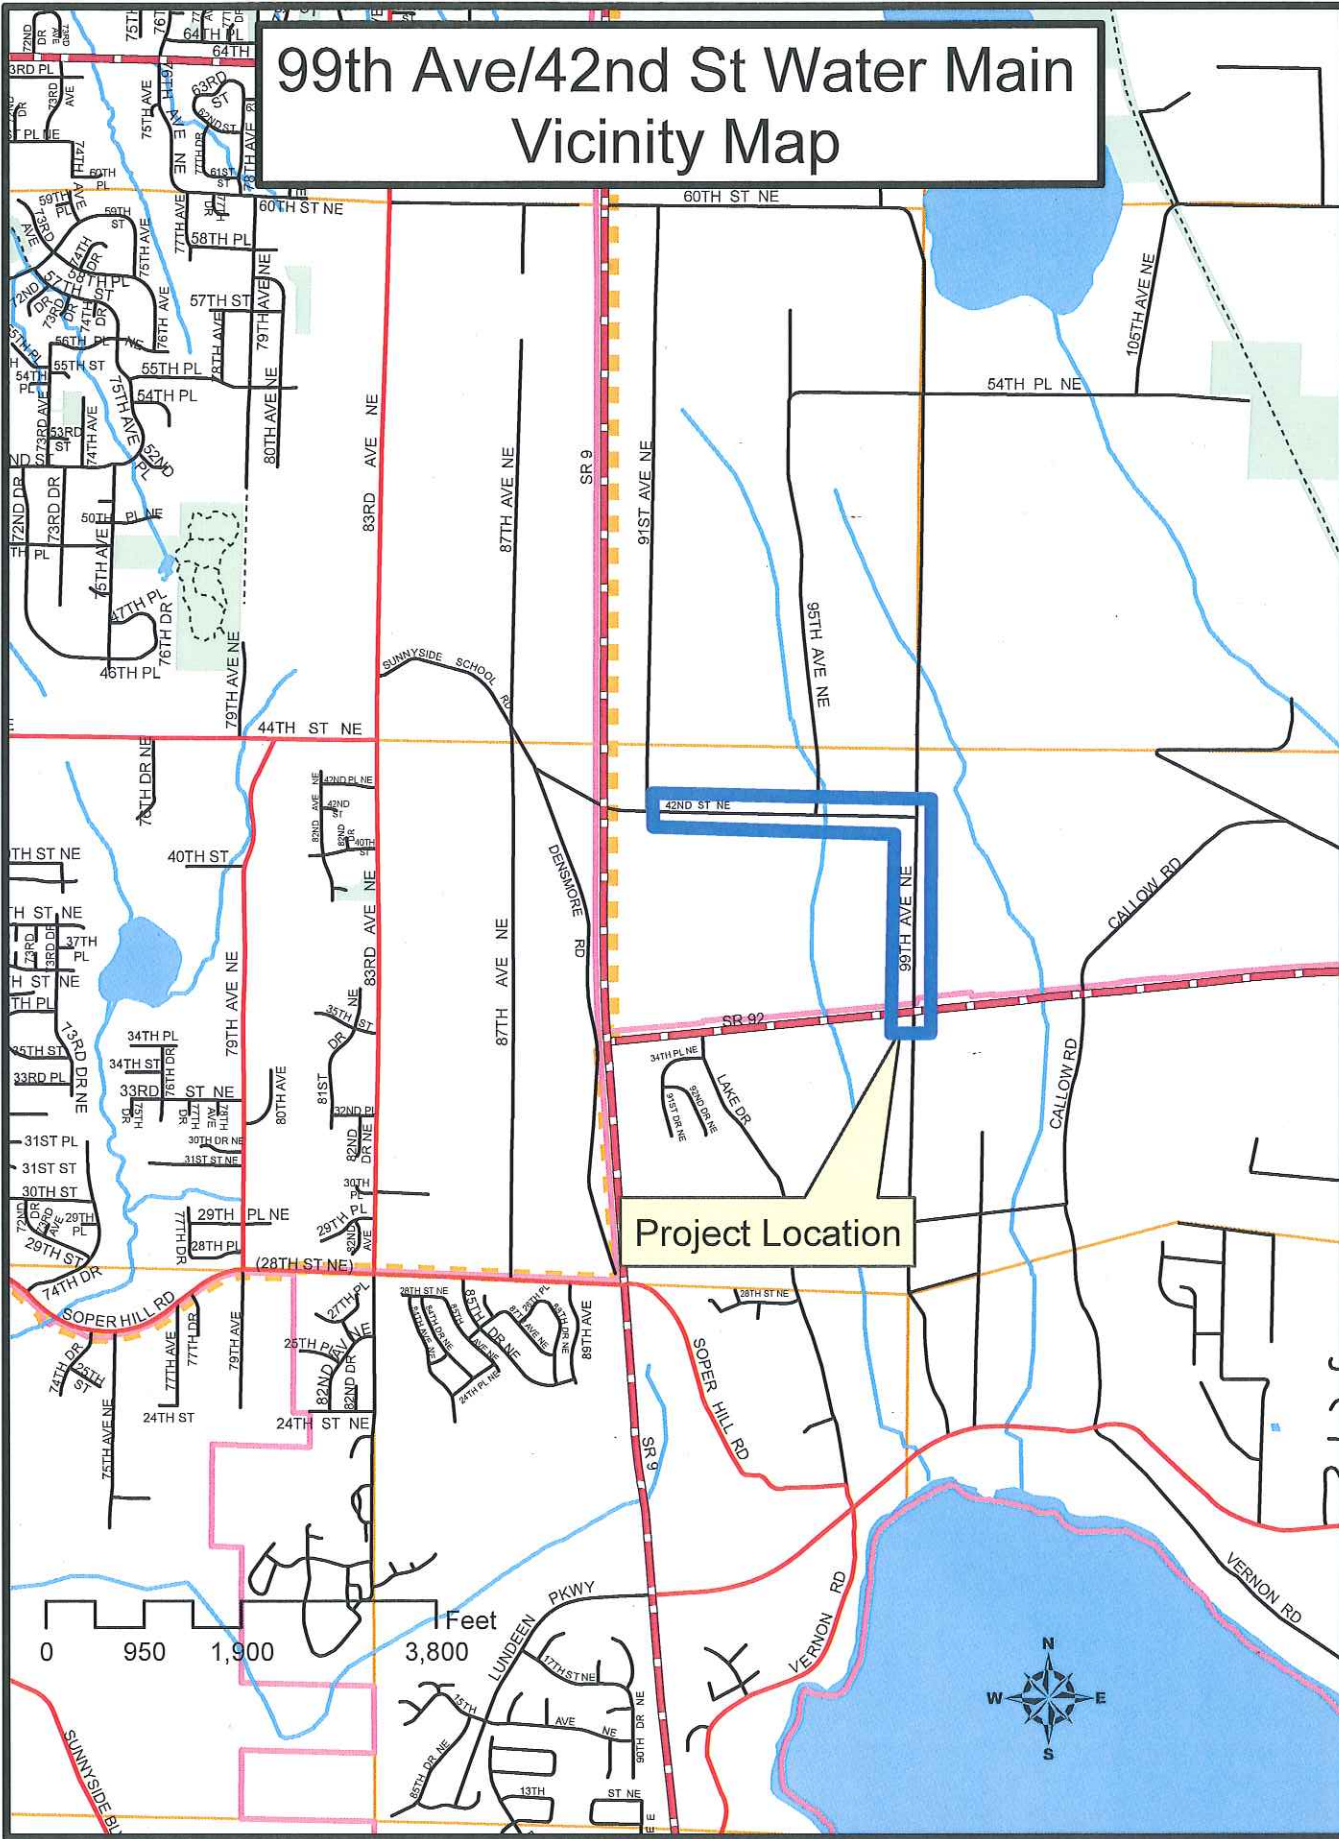

Project Location

0 950 1,900 3,800 Feet

