


**CITY OF MARYSVILLE AGENDA BILL**  
**EXECUTIVE SUMMARY FOR ACTION**

**CITY COUNCIL MEETING DATE: July 13, 2015**

|  |  |
|--|--|
| <b>AGENDA ITEM:</b><br>Project Acceptance – 88 <sup>th</sup> St NE and 55 <sup>th</sup> Ave NE Intersection Improvements |  |
| <b>PREPARED BY:</b><br>Jeff Laycock, Project Manager   | <b>DIRECTOR APPROVAL:</b><br> |
| <b>DEPARTMENT:</b><br>Engineering  |  |
| <b>ATTACHMENTS:</b><br>Notice of Physical Completion Letter, Vicinity Map  |  |
| <b>BUDGET CODE:</b><br>30500030.563000, R1303 (Roadway Improvements)<br>40220594.563000, W1401 (Water Main Improvements) | <b>AMOUNT:</b><br>N/A  |

**SUMMARY:**

The 88<sup>th</sup> St NE and 55<sup>th</sup> Ave NE Intersection Improvements project included the construction of a signalized intersection with left turn pockets, illumination, sidewalk ramps, roadway widening and paving. The project also included replacing the existing water main within the project limits.

City Council awarded the project to SRV Construction on July 14, 2014 in the amount of \$780,559.64. The project was completed at a cost of \$807,351.22, which was \$26,791.58 or 3.43% above the original bid amount but within management reserve.


The total cost to the City towards construction was \$153,683.48. The remaining construction cost was funded in part by the FY2014 Transportation Improvement Board (TIB) Urban Arterial Program and Snohomish County mitigation fees for 88<sup>th</sup> St NE improvements.

Work performed under this contract was inspected by City staff. The work was found to be physically complete in accordance with the approved plans and specifications. Staff recommends Council's acceptance of the project for closeout.

**RECOMMENDED ACTION:**

Staff recommends that Council authorize the Mayor to accept the 88<sup>th</sup> St NE and 55<sup>th</sup> Ave NE Intersection Improvements project, starting the 45-day lien filing period for project closeout.

# VICINITY MAP

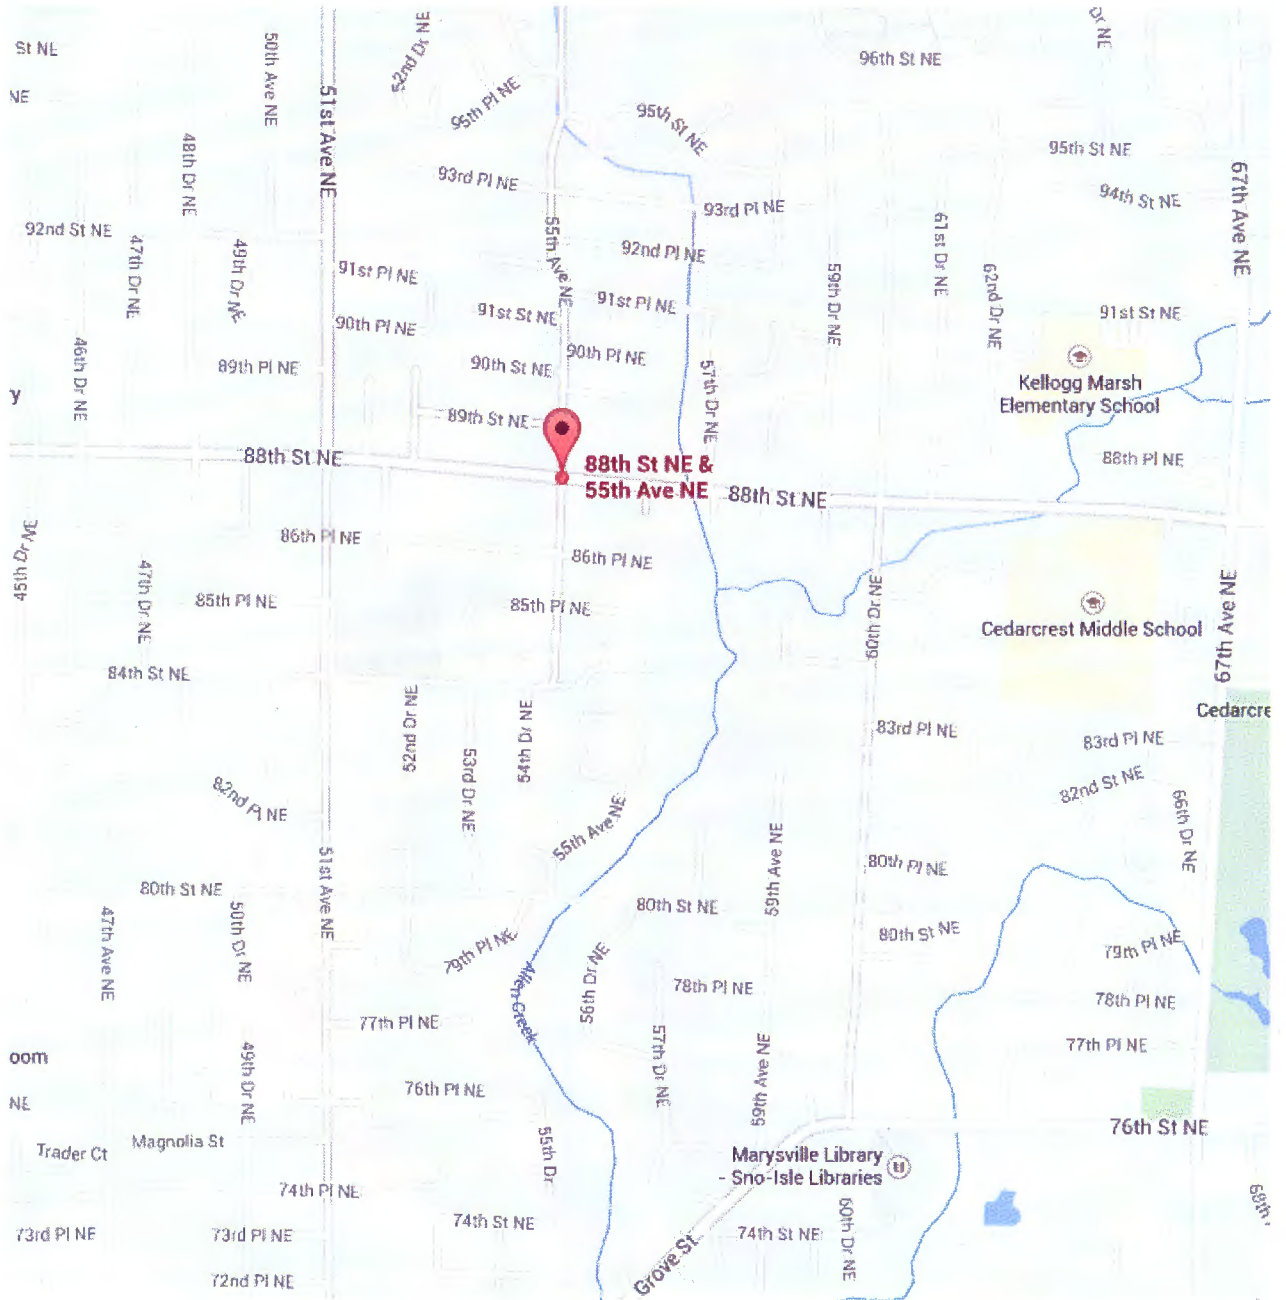



## **PUBLIC WORKS**

Kevin Nielsen, *Director*

80 Columbia Avenue  
Marysville, Washington 98270  
Phone (360) 363-8100  
Fax (360) 363-8284  
marysvillewa.gov

June 24, 2015

SRV Construction, Inc.  
PO Box 481  
Oak Harbor, WA 98277

**Subject: 88<sup>th</sup> St NE and 55<sup>th</sup> Ave NE Intersection Improvements – Notice of Physical Completion**

Dear Mr. Snyder:

In accordance with Section 1-05.11(2) of the Special Provisions, this project was considered physically complete as of Friday, June 12, 2015.

This notification does not constitute completion, or final acceptance by the City per Section 1-05.11(2) of the Contract's General Special Provisions.

Recommendation for Final Acceptance will be sent to the City Council for approval at the first available council meeting pending the above items to close out the project have been completed. This date of final acceptance shall start the forty-five (45) day lien period for the release of your retainage upon receipt of the following.

1. Certificate of Release from the Department of Revenue
2. Certificate of Release from the Employment Security Department
3. Certificate of Release from the Department of L&I
4. Affidavit of Wages Paid (to be submitted by SRV to the City)

As always, it has been a pleasure working with you and the rest of the SRV staff on this project. I look forward to working with you on future projects.

Sincerely,

A handwritten signature in blue ink, appearing to read "Jeff Laycock".

Jeff Laycock, PE  
Project Manager
